

LSJ CONSTRUCTION
Subcontractor Payout

Project: Laundry
Trade: Stone Veneer

October 21, 2010

Requisition #02

Subcontractor **Stephen Auguste**

Insurance expiration:


Invoice #	Requisition #02	Partial	Final
Phase #	04-450	-	X

Original Contract Sum:	\$26,000.00
Change Orders Submitted & Approved:	(\$5,000.00)
New Change Orders:	\$0.00
Total Work Contracted to Date:	\$21,000.00
Total Work Completed to Date:	✓ 98% \$20,580.00
Less Retainage:	\$0.00
Total Payments Made to Date:	\$13,230.00 ✓
Total Current Payment Due:	\$7,350.00 ✓OK
Balance to Finish including Retainage:	\$420.00

Sales Tax Liability:

- a. Subcontractor/Supplier is liable, explain **install only / tax included in contract**
- b. Non-resident Subcontractor/Supplier Bond Applicable:
- c. Use Tax to be paid by our company:
- d. Shipping **None**

Total Outlays for this contract incl. Sales or Use Tax: \$20,580.00

<p>JEE approval attached</p> <p>YES NO</p> <p> X</p>	<p>Invoice Attached</p> <p>YES NO</p> <p>X </p>
<p>Submitted Bill</p> <p>Signed: </p> <p>Date: October 21, 2010</p>	<p>Approved by: Gary </p> <p>Signed:</p> <p>Date: October 21, 2010</p>
<p>Approved by: Emad</p> <p>Signed: </p> <p>Date: 10/21/10</p>	<p>Approved by:</p> <p>Signed:</p> <p>Date:</p>

Stephen Auguste



October 18, 2010

Requisition #2
Period through 10-18-10

Payment requested for the installation of 210 face feet of stone veneer on the Laundry Room on Little St. James Island.

210 feet x \$35 = \$7,350.00


Thank you

Req. #1	378 f/ft	\$13,230.00
Req. #2	210 f/ft	\$ 7,350.00
Totals	588 f/ft	\$20,580.00

Tyson

10/18

STONE WORK AT LAUNDRY
SOUTH WALL TOTAL 210 SQ FT

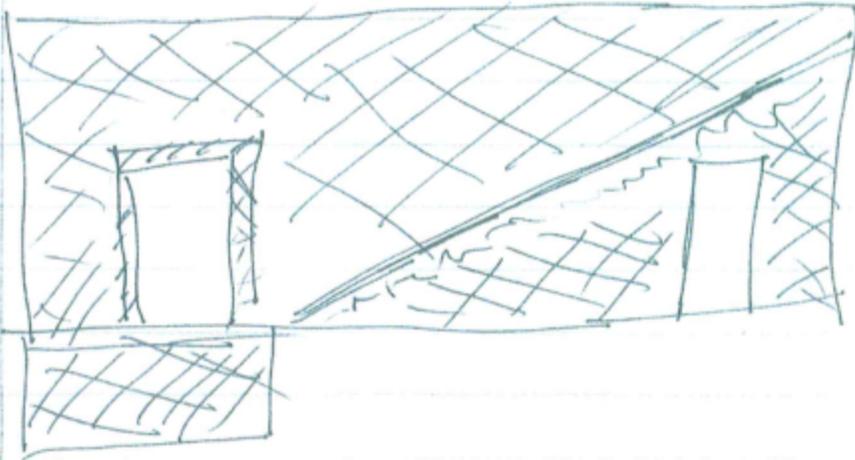

Upper 123 SQ FT

Lower 87 SQ FT

210 SQ FT

This completes work
on Laundry room

JM

10-19-10

Emad Hanna

From: Monique Harry [REDACTED]
Sent: Thursday, October 21, 2010 1:54 PM
To: Emad Hanna
Subject: Stephen Auguste
Attachments: Stephen Auguste 1006 Req 2.pdf

Emad,

Attached for payment Stephen Auguste Req 2 in the amount of \$7,350.00. Project 1006 code 04-450.

Monique
