


ALL ISLAND PROJECTS
AS OF 5/31/11

ID	Task Name	Duration	Start	Finish	June							July				August	
					5/22	5/29	6/5	6/12	6/19	6/26	7/3	7/10	7/17	7/24	7/31		
1	Flagpole Pool	91 days	Sun 5/29/11	Fri 9/30/11													
2	Main House Pool	97 days	Sun 5/29/11	Mon 10/10/11													
3	Cottage #4	97 days	Sun 5/29/11	Mon 10/10/11													
4	Relax Room	11 days	Sun 5/29/11	Fri 6/10/11													
5	Relax Restroom	60 days	Mon 6/13/11	Fri 9/2/11													
6																	
7	Paint Desal	30 days	Mon 6/13/11	Fri 7/22/11													
8	Desal Roof Waterproofing	20 days	Mon 7/25/11	Fri 8/19/11													
9	Mechanical Sitework	40 days	Mon 8/22/11	Fri 10/14/11													
10	Decommission Mechanical	25 days	Mon 10/17/11	Fri 11/18/11													
11																	
12	Terrace Wall	40 days	Sun 5/29/11	Thu 7/21/11													
13	Terrace Sea Wall	30 days	Fri 7/15/11	Thu 8/25/11													
14	Upper Terrace	30 days	Mon 8/8/11	Fri 9/16/11													
15	Roundabout	30 days	Fri 8/26/11	Thu 10/6/11													
16	Basket-Intersection Road	30 days	Fri 10/7/11	Thu 11/17/11													
17	Flagpole Road	30 days	Fri 10/14/11	Thu 11/24/11													
18	Helipad Road	20 days	Fri 11/25/11	Thu 12/22/11													
19																	
20	Five Palms	91 days	Mon 8/1/11	Mon 12/5/11													
21	Dock Shelters	40 days	Mon 9/5/11	Fri 10/28/11													
22	Manager's Cottage	60 days	Mon 8/22/11	Fri 11/11/11													
23																	
24	East Shelter	30 days	Mon 10/3/11	Fri 11/11/11													
25	Staff Restroom	40 days	Tue 10/11/11	Mon 12/5/11													
26	Helipad Wall	20 days	Mon 9/5/11	Fri 9/30/11													
27	Top of the Hill	70 days	Mon 8/1/11	Fri 11/4/11													

Project: All Jobs Schedule 29 June11
Date: Fri 7/1/11

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

ALL ISLAND PROJECTS
AS OF 5/31/11

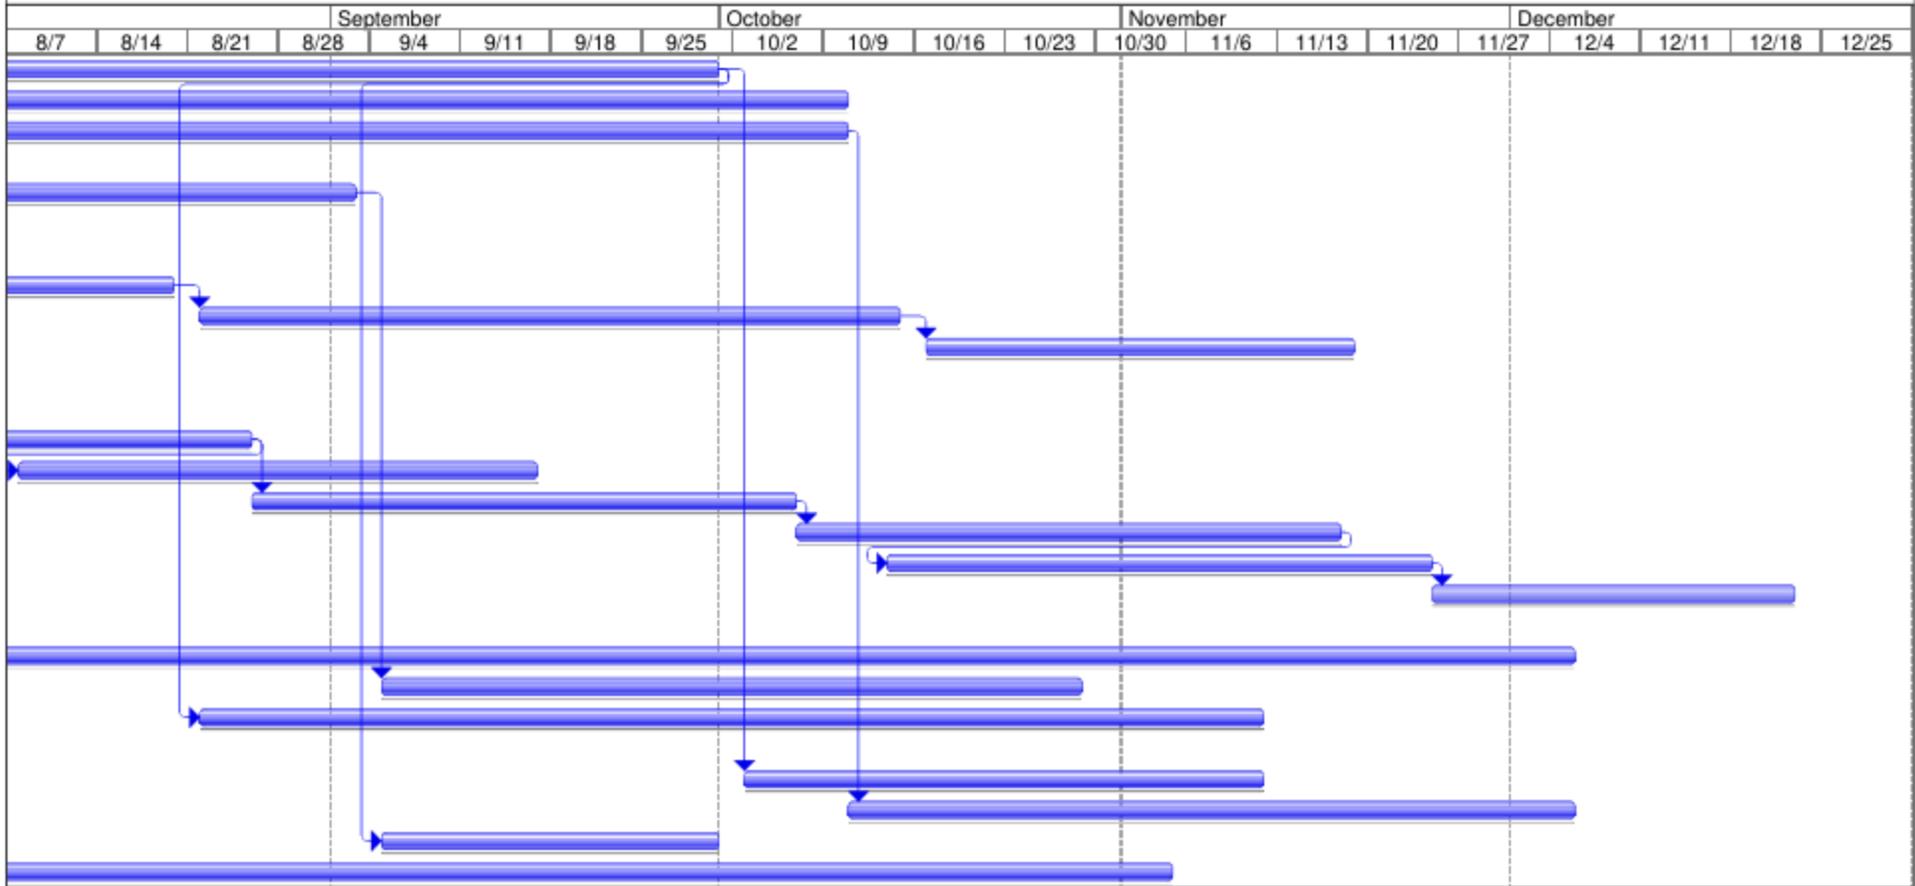

Project: All Jobs Schedule 29 June11
Date: Fri 7/1/11

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
