

#1011
MAIN HOUSE POOL


ID	Task Name	Duration	Start	Finish	Predecessors	May						
						4/10	4/17	4/24	5/1	5/8	5/15	5/22
1	Procurement	60 days	Mon 4/18/11	Fri 7/8/11								
2	Site design	30 days	Mon 4/18/11	Fri 5/27/11								
3	Pool tile	32 days	Mon 4/18/11	Tue 5/31/11								
4	Site drains	40 days	Mon 4/18/11	Fri 6/10/11								
5	Coral tile	30 days	Mon 4/18/11	Fri 5/27/11								
6	Site lighting	40 days	Mon 4/18/11	Fri 6/10/11								
7	Rebar	15 days	Mon 4/18/11	Fri 5/6/11								
8	CMU	5 days	Mon 4/18/11	Fri 4/22/11								
9	Doors/Frames/Shutters	60 days	Mon 4/18/11	Fri 7/8/11								
10	Interior doors	60 days	Mon 4/18/11	Fri 7/8/11								
11	Finish hardware	60 days	Mon 4/18/11	Fri 7/8/11								
12	Roof framing	45 days	Mon 4/18/11	Fri 6/17/11								
13	Roofing assembly	40 days	Mon 4/18/11	Fri 6/10/11								
14	Copper gutters	20 days	Mon 4/18/11	Fri 5/13/11								
15	Shower enclosure	50 days	Mon 4/18/11	Fri 6/24/11								
16	Coral flooring	30 days	Mon 4/18/11	Fri 5/27/11								
17	Vanity / Tops	45 days	Mon 4/18/11	Fri 6/17/11								
18	Plumbing fixtures	45 days	Mon 4/18/11	Fri 6/17/11								
19	A/C Systems	45 days	Mon 4/18/11	Fri 6/17/11								
20	Electrical fixtures	45 days	Mon 4/18/11	Fri 6/17/11								
21												
22												
23	Sitework	105 days	Mon 4/18/11	Fri 9/9/11								
24	Underground utilities	15 days	Mon 4/18/11	Fri 5/6/11								
25	Pool tile	12 days	Wed 6/1/11	Thu 6/16/11	3							
26	Diamond brite	12 days	Fri 6/17/11	Mon 7/4/11	25							
27	Complete pool	0 days	Mon 7/4/11	Mon 7/4/11	26							
28	Drainage	10 days	Mon 6/13/11	Fri 6/24/11	4							
29	Pool deck	20 days	Mon 6/27/11	Fri 7/22/11	28							
30	Coral tile	20 days	Mon 7/11/11	Fri 8/5/11	29FS-10 days							
31	Stone walls	30 days	Mon 7/11/11	Fri 8/19/11	29FS-10 days							
32	Finish grade	5 days	Mon 8/22/11	Fri 8/26/11	31							
33	Landscaping	5 days	Mon 8/29/11	Fri 9/2/11	32							
34	Site lighting	10 days	Mon 8/29/11	Fri 9/9/11	32							
35												
36												
37	Cottage #4	147 days	Mon 4/18/11	Tue 11/8/11								
38	Basement walls	15 days	Mon 4/18/11	Fri 5/6/11								
39	Elevated slab	10 days	Mon 5/9/11	Fri 5/20/11	38							
40	Waterproofing	2 days	Mon 5/9/11	Tue 5/10/11	38							

Project: 1011 Update15Jul11
Date: Mon 7/18/11

Critical		Baseline		Project Summary	
Critical Split		Baseline Split		External Tasks	
Critical Progress		Baseline Milestone		External Milestone	
Task		Milestone		Deadline	
Split		Summary Progress			
Task Progress		Summary			

#1011
MAIN HOUSE POOL


ID	Task Name	Duration	Start	Finish	Predecessors	May						
						4/10	4/17	4/24	5/1	5/8	5/15	5/22
41	Foundation drain	2 days	Mon 5/9/11	Tue 5/10/11	38							
42	Cottage #4 backfill	3 days	Wed 5/11/11	Fri 5/13/11	41							
43	CMU	30 days	Mon 6/6/11	Fri 7/15/11	39FS+10 days							
44	Roof framing	10 days	Mon 7/18/11	Fri 7/29/11	43							
45	Roof assembly	20 days	Mon 8/1/11	Fri 8/26/11	44							
46	Copper gutters	5 days	Mon 8/22/11	Fri 8/26/11	45FS-5 days							
47	Downspouts	2 days	Mon 8/29/11	Tue 8/30/11	45							
48	Stone veneer	30 days	Mon 8/15/11	Fri 9/23/11	45FS-10 days							
49	Set door frames	3 days	Mon 8/29/11	Wed 8/31/11	45							
50	Interior framing	5 days	Mon 8/29/11	Fri 9/2/11	45							
51	Interior plaster	15 days	Mon 9/5/11	Fri 9/23/11	50							
52	Interior doors	5 days	Mon 9/5/11	Fri 9/9/11	50							
53	Bathroom tile	5 days	Mon 9/26/11	Fri 9/30/11	51							
54	Shower enclosure	1 day	Mon 10/3/11	Mon 10/3/11	53							
55	Vanity / Tops	2 days	Mon 10/3/11	Tue 10/4/11	53							
56	Accessories	2 days	Tue 10/4/11	Wed 10/5/11	54							
57	Interior painting	5 days	Mon 9/26/11	Fri 9/30/11	51							
58	Flooring	5 days	Mon 10/3/11	Fri 10/7/11	57							
59	Plumbing Rough	5 days	Mon 9/5/11	Fri 9/9/11	50							
60	Plumbing Finish	5 days	Wed 10/5/11	Tue 10/11/11	55							
61	A/C Systems	30 days	Mon 9/5/11	Fri 10/14/11	50							
62	Electrical Rough	5 days	Mon 9/5/11	Fri 9/9/11	50							
63	Electrical Finish	5 days	Mon 10/10/11	Fri 10/14/11	58							
64	Decorative Painting	10 days	Mon 10/17/11	Fri 10/28/11	63							
65	Punch List	3 days	Mon 10/31/11	Wed 11/2/11	64							
66	Clean up	2 days	Thu 11/3/11	Fri 11/4/11	65							
67	Inspection	1 day	Mon 11/7/11	Mon 11/7/11	66							
68	Furnishings	1 day	Tue 11/8/11	Tue 11/8/11	67							
69	Completion	0 days	Tue 11/8/11	Tue 11/8/11	68							



Project: 1011 Update15Jul11
Date: Mon 7/18/11

Critical		Baseline		Project Summary	
Critical Split		Baseline Split		External Tasks	
Critical Progress		Baseline Milestone		External Milestone	
Task		Milestone		Deadline	
Split		Summary Progress			
Task Progress		Summary			


#1011
MAIN HOUSE POOL

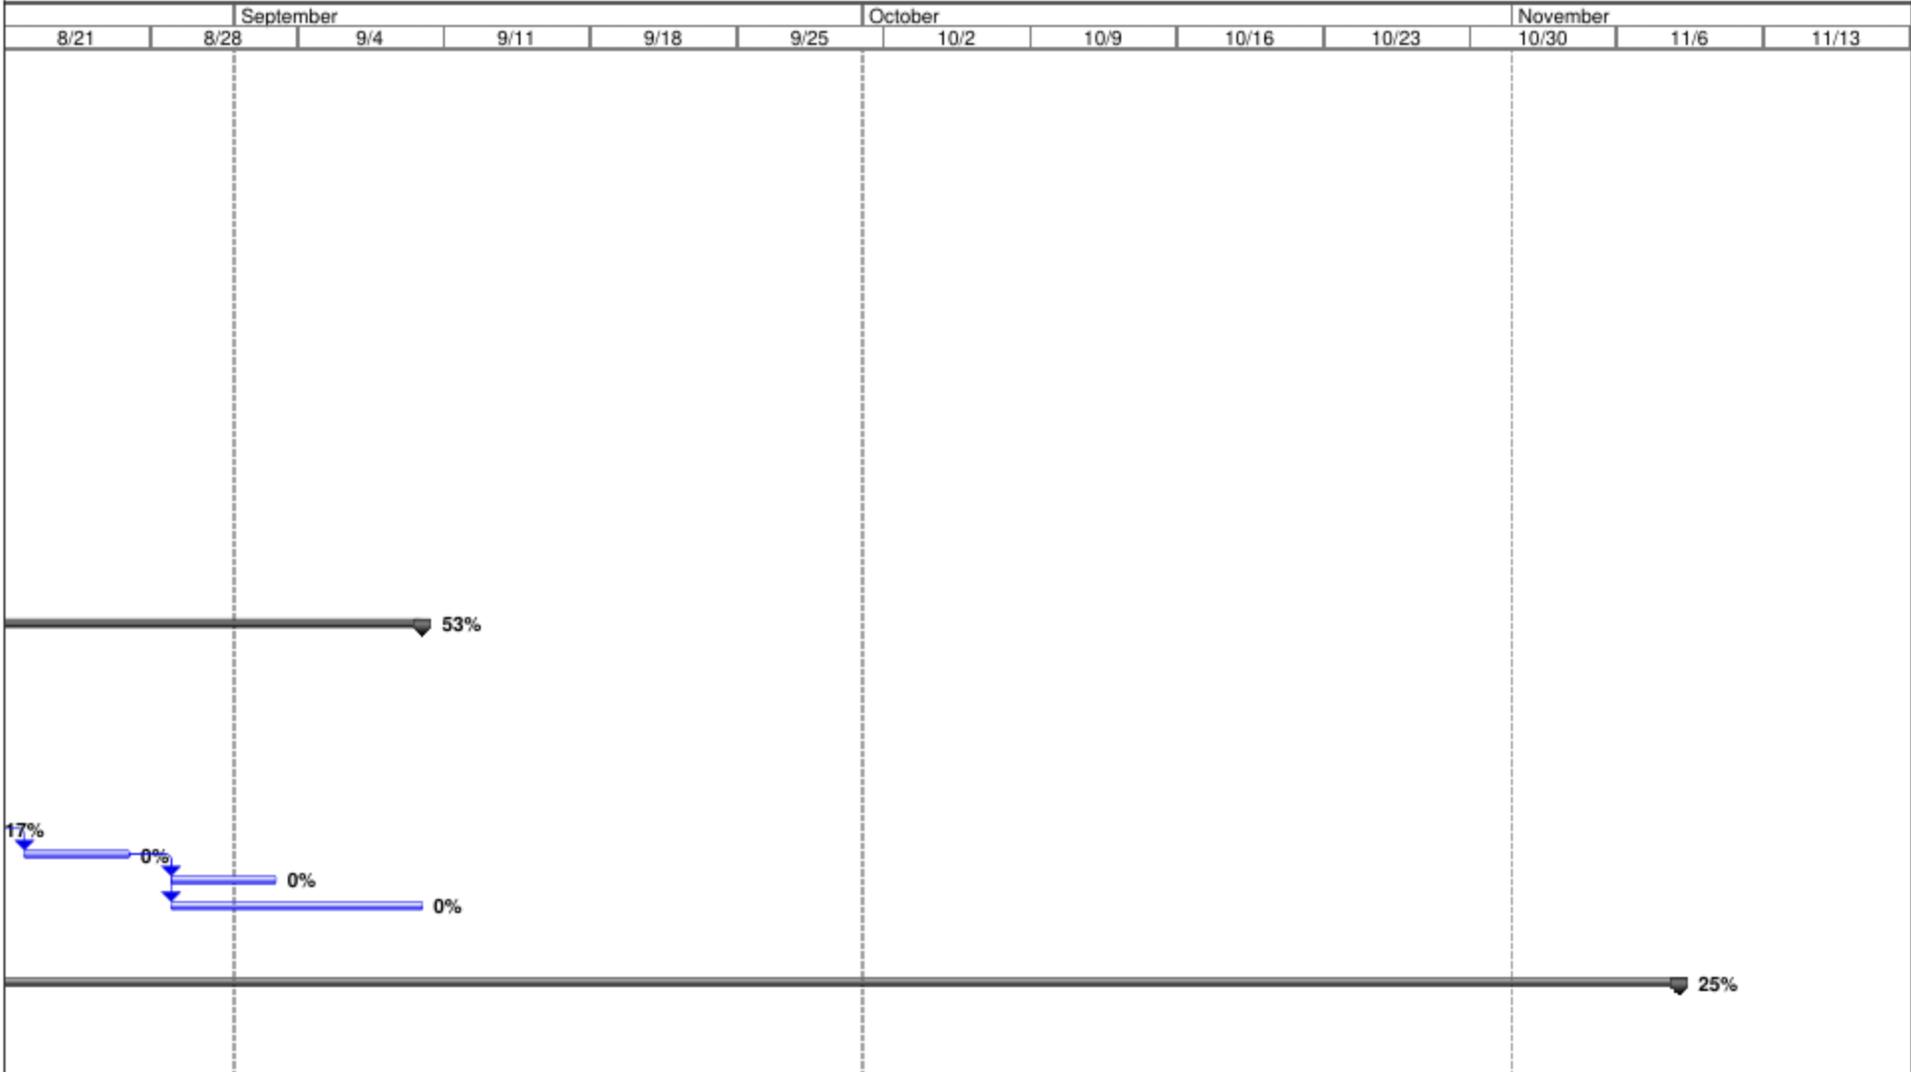

Project: 1011 Update15Jul11
Date: Mon 7/18/11

Critical		Baseline		Project Summary	
Critical Split		Baseline Split		External Tasks	
Critical Progress		Baseline Milestone		External Milestone	
Task		Milestone		Deadline	
Split		Summary Progress			
Task Progress		Summary			

#1011
MAIN HOUSE POOL

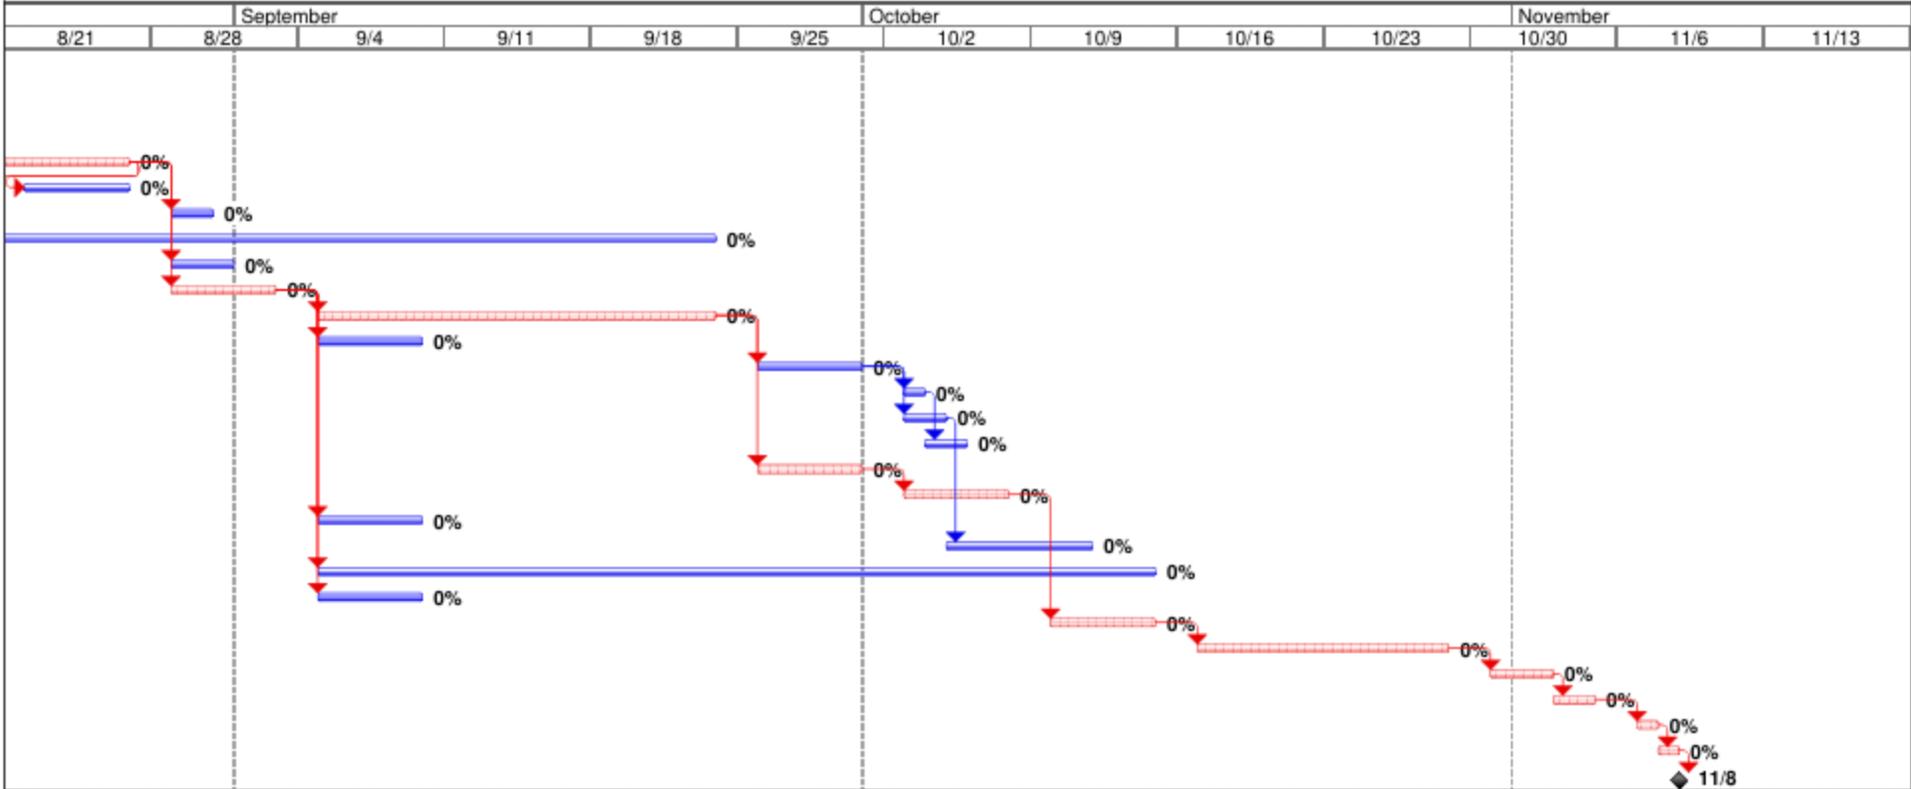

Project: 1011 Update15Jul11 Date: Mon 7/18/11	Critical		Baseline		Project Summary	
	Critical Split		Baseline Split		External Tasks	
	Critical Progress		Baseline Milestone		External Milestone	
	Task		Milestone		Deadline	
	Split		Summary Progress			
Task Progress		Summary				
