

#1013
FLAGPOLE POOL


ID	Task Name	Duration	Start	Finish	May						
					4/10	4/17	4/24	5/1	5/8	5/15	5/22
1	Procurement	75 days	Mon 4/18/11	Fri 7/29/11							
2	Trench drain	20 days	Mon 4/18/11	Fri 5/13/11							
3	Site lighting	75 days	Mon 4/18/11	Fri 7/29/11							
4	Coral tiles	15 days	Mon 4/18/11	Fri 5/6/11							
5	Pool tiles	30 days	Mon 4/18/11	Fri 5/27/11							
6	Roof trusses	15 days	Mon 4/18/11	Fri 5/6/11							
7	Roof tiles	25 days	Mon 4/18/11	Fri 5/20/11							
8	Exterior doors	45 days	Mon 4/18/11	Fri 6/17/11							
9	Interior doors	45 days	Mon 4/18/11	Fri 6/17/11							
10	Finish hardware	45 days	Mon 4/18/11	Fri 6/17/11							
11	Shower enclosure	75 days	Mon 4/18/11	Fri 7/29/11							
12	Bathroom tile	65 days	Mon 4/18/11	Fri 7/15/11							
13	Flooring	45 days	Mon 4/18/11	Fri 6/17/11							
14	Hurricane shutter	15 days	Mon 4/18/11	Fri 5/6/11							
15	Sun shade	45 days	Mon 4/18/11	Fri 6/17/11							
16	Kitchen equipment	75 days	Mon 4/18/11	Fri 7/29/11							
17	Cabinets / Tops	50 days	Mon 4/18/11	Fri 6/24/11							
18	Plumbing fixtures	45 days	Mon 4/18/11	Fri 6/17/11							
19	A/C Systems	40 days	Mon 4/18/11	Fri 6/10/11							
20	Electrical fixtures	45 days	Mon 4/18/11	Fri 6/17/11							
21											
22	Sitework	110 days	Mon 4/18/11	Fri 9/16/11							
23	Rough Site	10 days	Mon 4/18/11	Fri 4/29/11							
24	Underground utilities	30 days	Mon 4/18/11	Fri 5/27/11							
25	Install trench drain	20 days	Mon 5/16/11	Fri 6/10/11							
26	Pool deck concrete	25 days	Mon 5/16/11	Fri 6/17/11							
27	Pool deck tile	50 days	Mon 6/20/11	Fri 8/26/11							
28	Site lighting	5 days	Mon 9/12/11	Fri 9/16/11							
29	Site concrete	40 days	Mon 5/2/11	Fri 6/24/11							
30	Complete pool	15 days	Mon 5/30/11	Fri 6/17/11							
31	Stonework	60 days	Mon 6/6/11	Fri 8/26/11							
32	Finish grade	5 days	Mon 8/29/11	Fri 9/2/11							
33	Landscaping	5 days	Mon 9/5/11	Fri 9/9/11							
34	Sun structures	45 days	Mon 6/27/11	Fri 8/26/11							
35											
36	Exterior	128 days?	Mon 4/18/11	Wed 10/12/11							
37	Poolhouse CMU	10 days	Mon 4/18/11	Fri 4/29/11							
38	Roof truss system	5 days	Mon 5/9/11	Fri 5/13/11							
39	Roof close in	45 days	Mon 5/16/11	Fri 7/15/11							
40	Roof Tile	10 days?	Mon 7/18/11	Fri 7/29/11							

Project: 1013Update 15Jul11
Date: Mon 7/18/11

Critical		Baseline		Project Summary	
Critical Split		Baseline Split		External Tasks	
Critical Progress		Baseline Milestone		External Milestone	
Task		Milestone		Deadline	
Split		Summary Progress			
Task Progress		Summary			

#1013
FLAGPOLE POOL


ID	Task Name	Duration	Start	Finish	May							
					4/10	4/17	4/24	5/1	5/8	5/15	5/22	
41	Gutter / Downspouts	5 days	Mon 7/11/11	Fri 7/15/11								
42	Set exterior doors	5 days	Wed 7/6/11	Tue 7/12/11								
43	Exterior stucco	40 days	Mon 5/16/11	Fri 7/8/11								
44	Exterior painting	5 days	Mon 7/18/11	Fri 7/22/11								
45	Hurricane shutter	1 day	Mon 7/25/11	Mon 7/25/11								
46	Sunshade	1 day	Tue 7/26/11	Tue 7/26/11								
47	Interior framing	5 days	Mon 5/2/11	Fri 5/6/11								
48	Interior plaster	15 days	Mon 7/4/11	Fri 7/22/11								
49	Venetian Plaster	10 days	Mon 7/25/11	Fri 8/5/11								
50	Interior doors	3 days	Mon 8/8/11	Wed 8/10/11								
51	Bathroom tile	15 days	Mon 8/1/11	Fri 8/19/11								
52	Flooring	10 days	Mon 8/22/11	Fri 9/2/11								
53	Shower enclosure	2 days	Mon 8/22/11	Tue 8/23/11								
54	Cabinets / Tops	5 days	Mon 8/22/11	Fri 8/26/11								
55	Accessories	3 days	Wed 8/24/11	Fri 8/26/11								
56	Kitchen equipment	2 days	Mon 8/29/11	Tue 8/30/11								
57	Interior painting	10 days	Mon 8/8/11	Fri 8/19/11								
58	Plumbing Rough	10 days	Mon 5/9/11	Fri 5/20/11								
59	Plumbing Finish	5 days	Wed 8/24/11	Tue 8/30/11								
60	A/C Systems	35 days	Mon 5/23/11	Fri 7/8/11								
61	Electrical Rough	10 days	Mon 5/9/11	Fri 5/20/11								
62	Electrical Finish	5 days	Wed 8/31/11	Tue 9/6/11								
63	Decorative Painting	15 days	Wed 9/7/11	Tue 9/27/11								
64	Punch List	3 days	Wed 9/28/11	Fri 9/30/11								
65	Clean up	2 days	Mon 10/3/11	Tue 10/4/11								
66	Inspection	1 day	Wed 10/5/11	Wed 10/5/11								
67	Furnishings	5 days	Thu 10/6/11	Wed 10/12/11								
68	Completion	0 days	Wed 10/12/11	Wed 10/12/11								

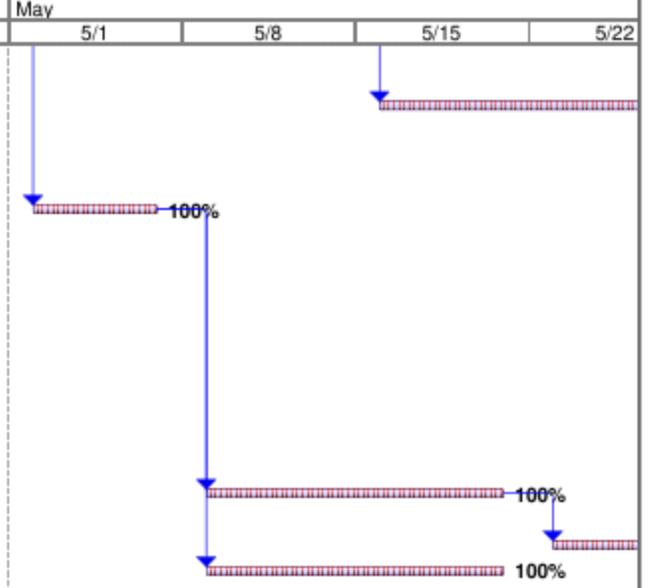

Project: 1013Update 15Jul11
Date: Mon 7/18/11


Critical		Baseline		Project Summary	
Critical Split		Baseline Split		External Tasks	
Critical Progress		Baseline Milestone		External Milestone	
Task		Milestone		Deadline	
Split		Summary Progress			
Task Progress		Summary			

#1013
FLAGPOLE POOL

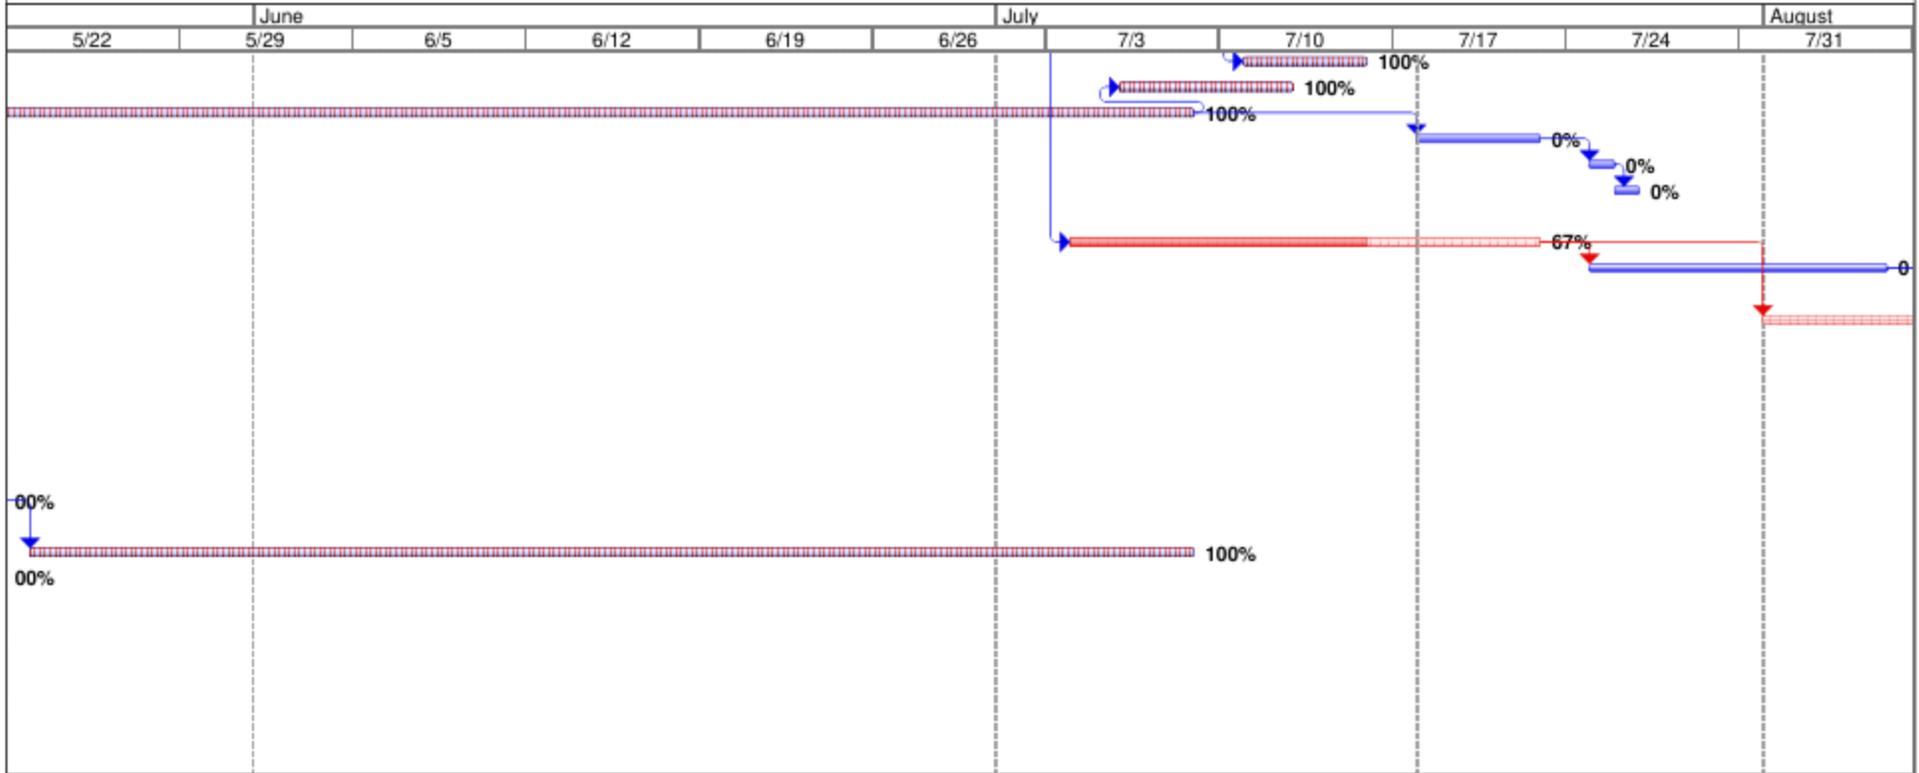

Project: 1013Update 15Jul11 Date: Mon 7/18/11	Critical		Baseline		Project Summary	
	Critical Split		Baseline Split		External Tasks	
	Critical Progress		Baseline Milestone		External Milestone	
	Task		Milestone		Deadline	
	Split		Summary Progress			
	Task Progress		Summary			


#1013
FLAGPOLE POOL

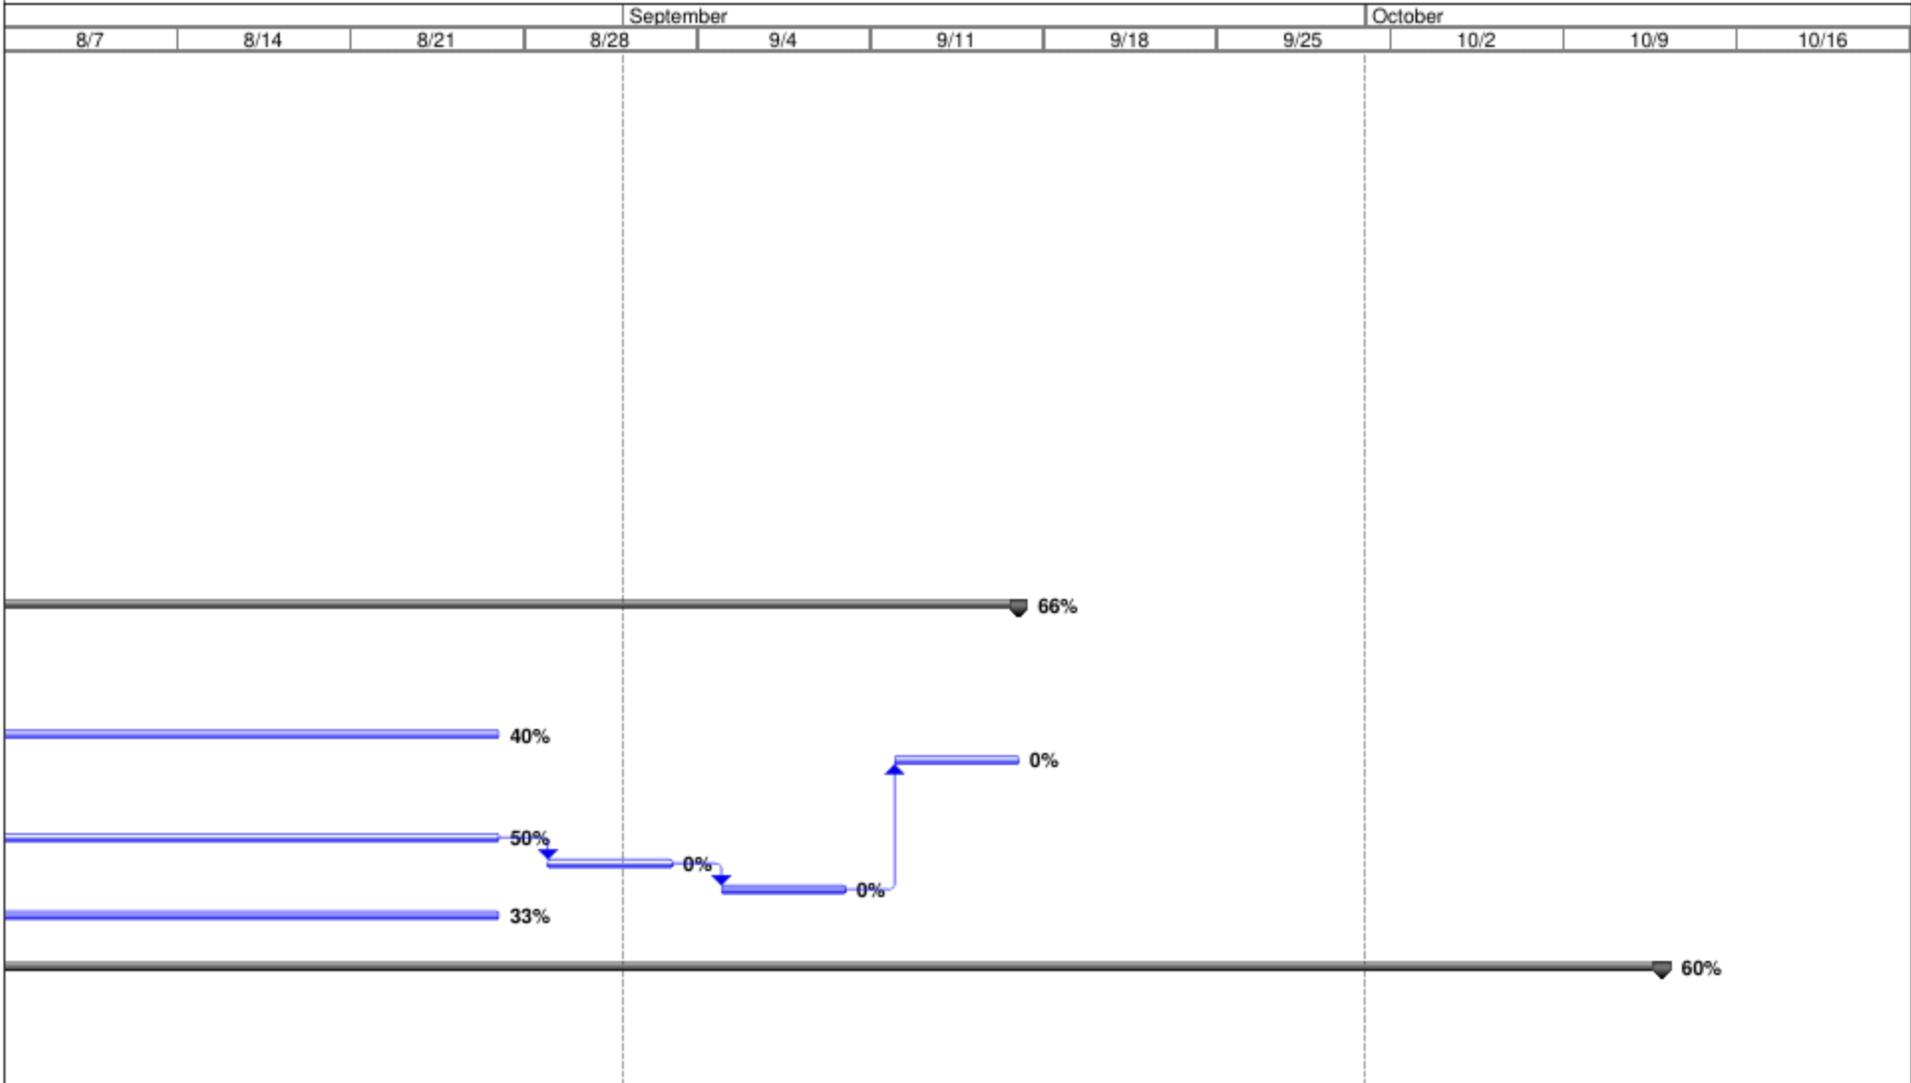

Project: 1013Update 15Jul11
Date: Mon 7/18/11

Critical		Baseline		Project Summary	
Critical Split		Baseline Split		External Tasks	
Critical Progress		Baseline Milestone		External Milestone	
Task		Milestone		Deadline	
Split		Summary Progress			
Task Progress		Summary			

#1013
FLAGPOLE POOL

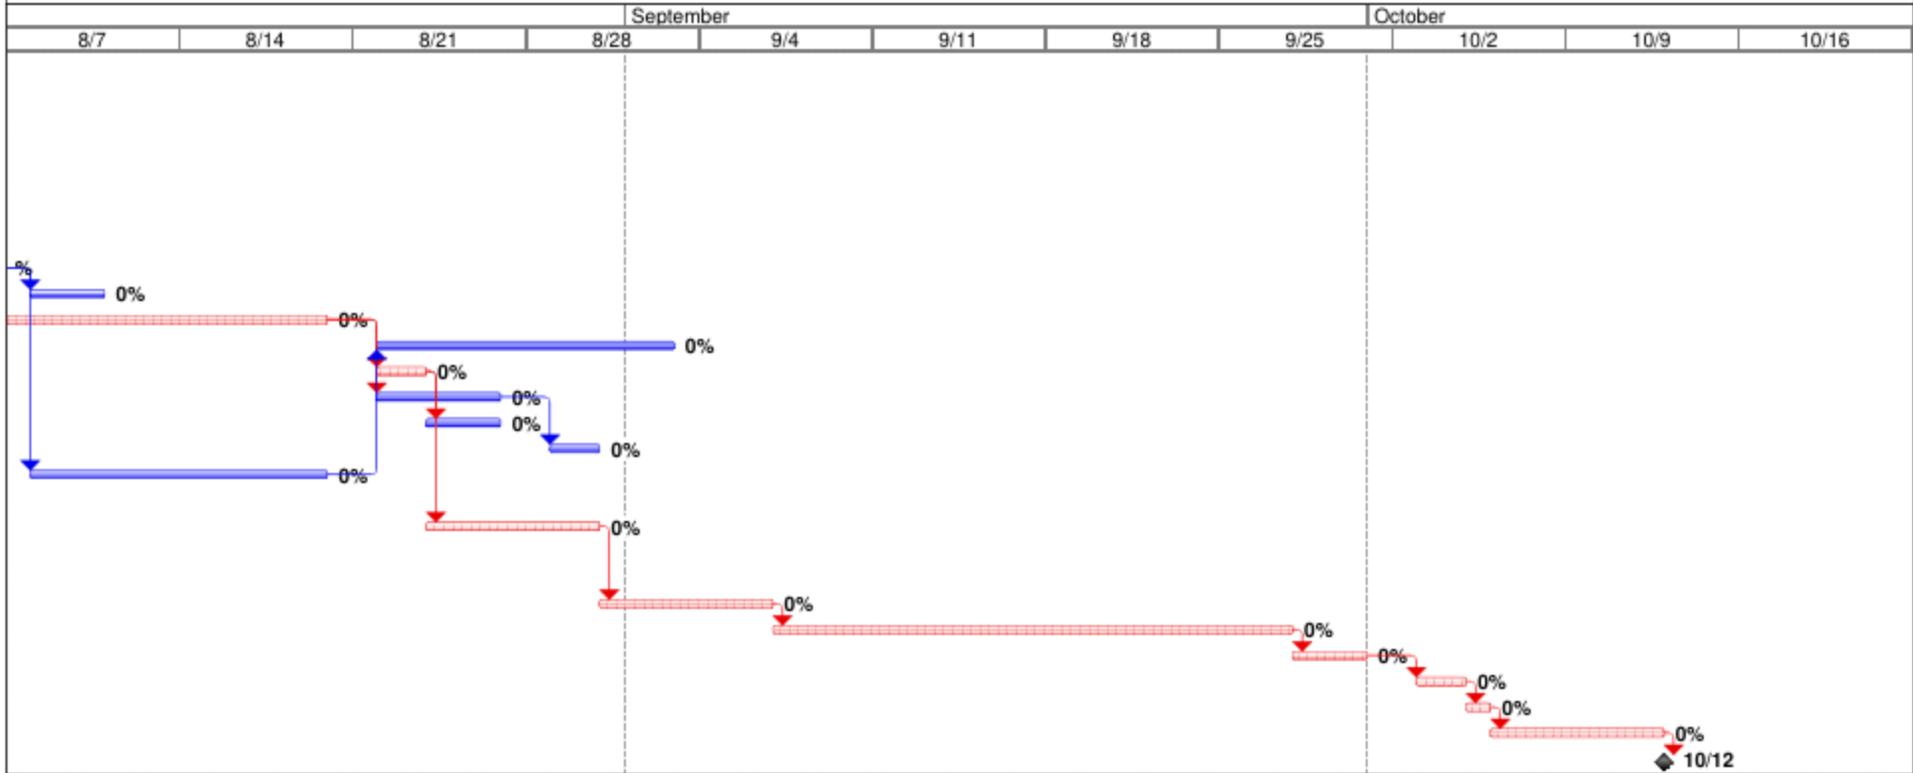

Project: 1013Update 15Jul11
Date: Mon 7/18/11

Critical		Baseline		Project Summary	
Critical Split		Baseline Split		External Tasks	
Critical Progress		Baseline Milestone		External Milestone	
Task		Milestone		Deadline	
Split		Summary Progress			
Task Progress		Summary			
