



# OLYMPIA STEEL BUILDINGS® SYSTEMS

400 Island Avenue, McKees Rocks, PA 15136

Web Site: [REDACTED]

Toll Free Phone: (888) 449-7756 Fax: (724)744-6062 Cell: 724-396-8269

## FACTORY DIRECT TO YOUR DOOR

Name: Daphne Wallace Date: 8/14/13  
 Address: \_\_\_\_\_ Company: \_\_\_\_\_  
 City: \_\_\_\_\_ State: \_\_\_\_\_ Zip: \_\_\_\_\_  
 Phone: \_\_\_\_\_ Fax: \_\_\_\_\_ Country: St. Thomas

### YOUR STEEL BUILDING SPECIFICATIONS

Width: 120'	Bay Spacing: 22'	Wall Color: color	Bldg Code: IBC
Length: 110'	Frame Type: H-Beam	Trim Color: color	Wind Load: 165 mph
Eave Ht: 35'	Roof Type: PBR 26 Ga.	Coating on Roof: Galvalume	Ground Snow: 0 psf
Roof Pitch: 1:12	Clearance Under Eaves: 30'	Coating On Walls: color	Exposure: C
Left Endwall: <input checked="" type="checkbox"/> Post & Beam	<input type="checkbox"/> Rigid FR 1/2 LD	<input type="checkbox"/> Full LD	Collateral Load: 1 psf
Right Endwall: <input checked="" type="checkbox"/> Post & Beam	<input type="checkbox"/> Rigid FR 1/2 LD	<input type="checkbox"/> Full LD	
Bracing: <input checked="" type="checkbox"/> Cable	<input type="checkbox"/> Portal	<input type="checkbox"/> Rod	Base Condition: Angle with base trim

Framed openings: 100x27

Gutters & Downspouts: included

Building designed to carry the weight of a 100x27 hangar door (hangar door by others)

6" roof and 6" wall insulation: Add \$19,426.00

6" roof and 4" wall insulation: Add \$17,605.00

### ALL BUILDINGS INCLUDE:

- 25 YEAR WARRANTY ON STAINLESS STEEL CAPPED SCREWS (NO RUST)
- 40 YEAR WARRANTY AGAINST CRACKING, CHIPPING OR PEELING ON POLYESTER BAKED PAINT ON SIDEWALLS
- GALVANIZED Z-GIRTS AND Z-PURLINS • WASHERS ON PANELS ON SIDES AND ROOF
- 26 GAUGE COLOR WALL SHEETING (10 AVAILABLE COLORS)
- STRUCTURAL STEEL I-BEAMS • ENDWALL POSTS • RAFTERS • NUTS • BOLTS • X-BRACING • COLOR TRIM
- 1" MASTIC TAPE FOR SIDE LAPS ON ROOF • 1" DOUBLE BEAD MASTIC FOR END LAPS ON ROOF
- CERTIFIED, ENGINEER STAMPED DRAWINGS TO MEET YOUR STATE AND COUNTY REQUIREMENTS

BUILDING PRICE.....	<b>\$275,337.00</b>
DELIVERY..to.Palm.Beach.port.only.....	<b>\$ included</b>
TAX.....	<b>\$ none</b>
TOTAL.....	<b>\$275,337.00</b>
DEPOSIT.....	<b>\$68,834.00</b>
BALANCE ON DELIVERY.....	<b>\$206,503.00</b>

**Price includes 3 sets of engineer stamped drawings and anchor bolt plans!!!!**


Price Quote is valid until this Date: 8/31/13

SINCERELY,

PHONE# (888) 449-7756 Ext. 257

Jill Leonello


## 25 YEAR FACTORY WARRANTY

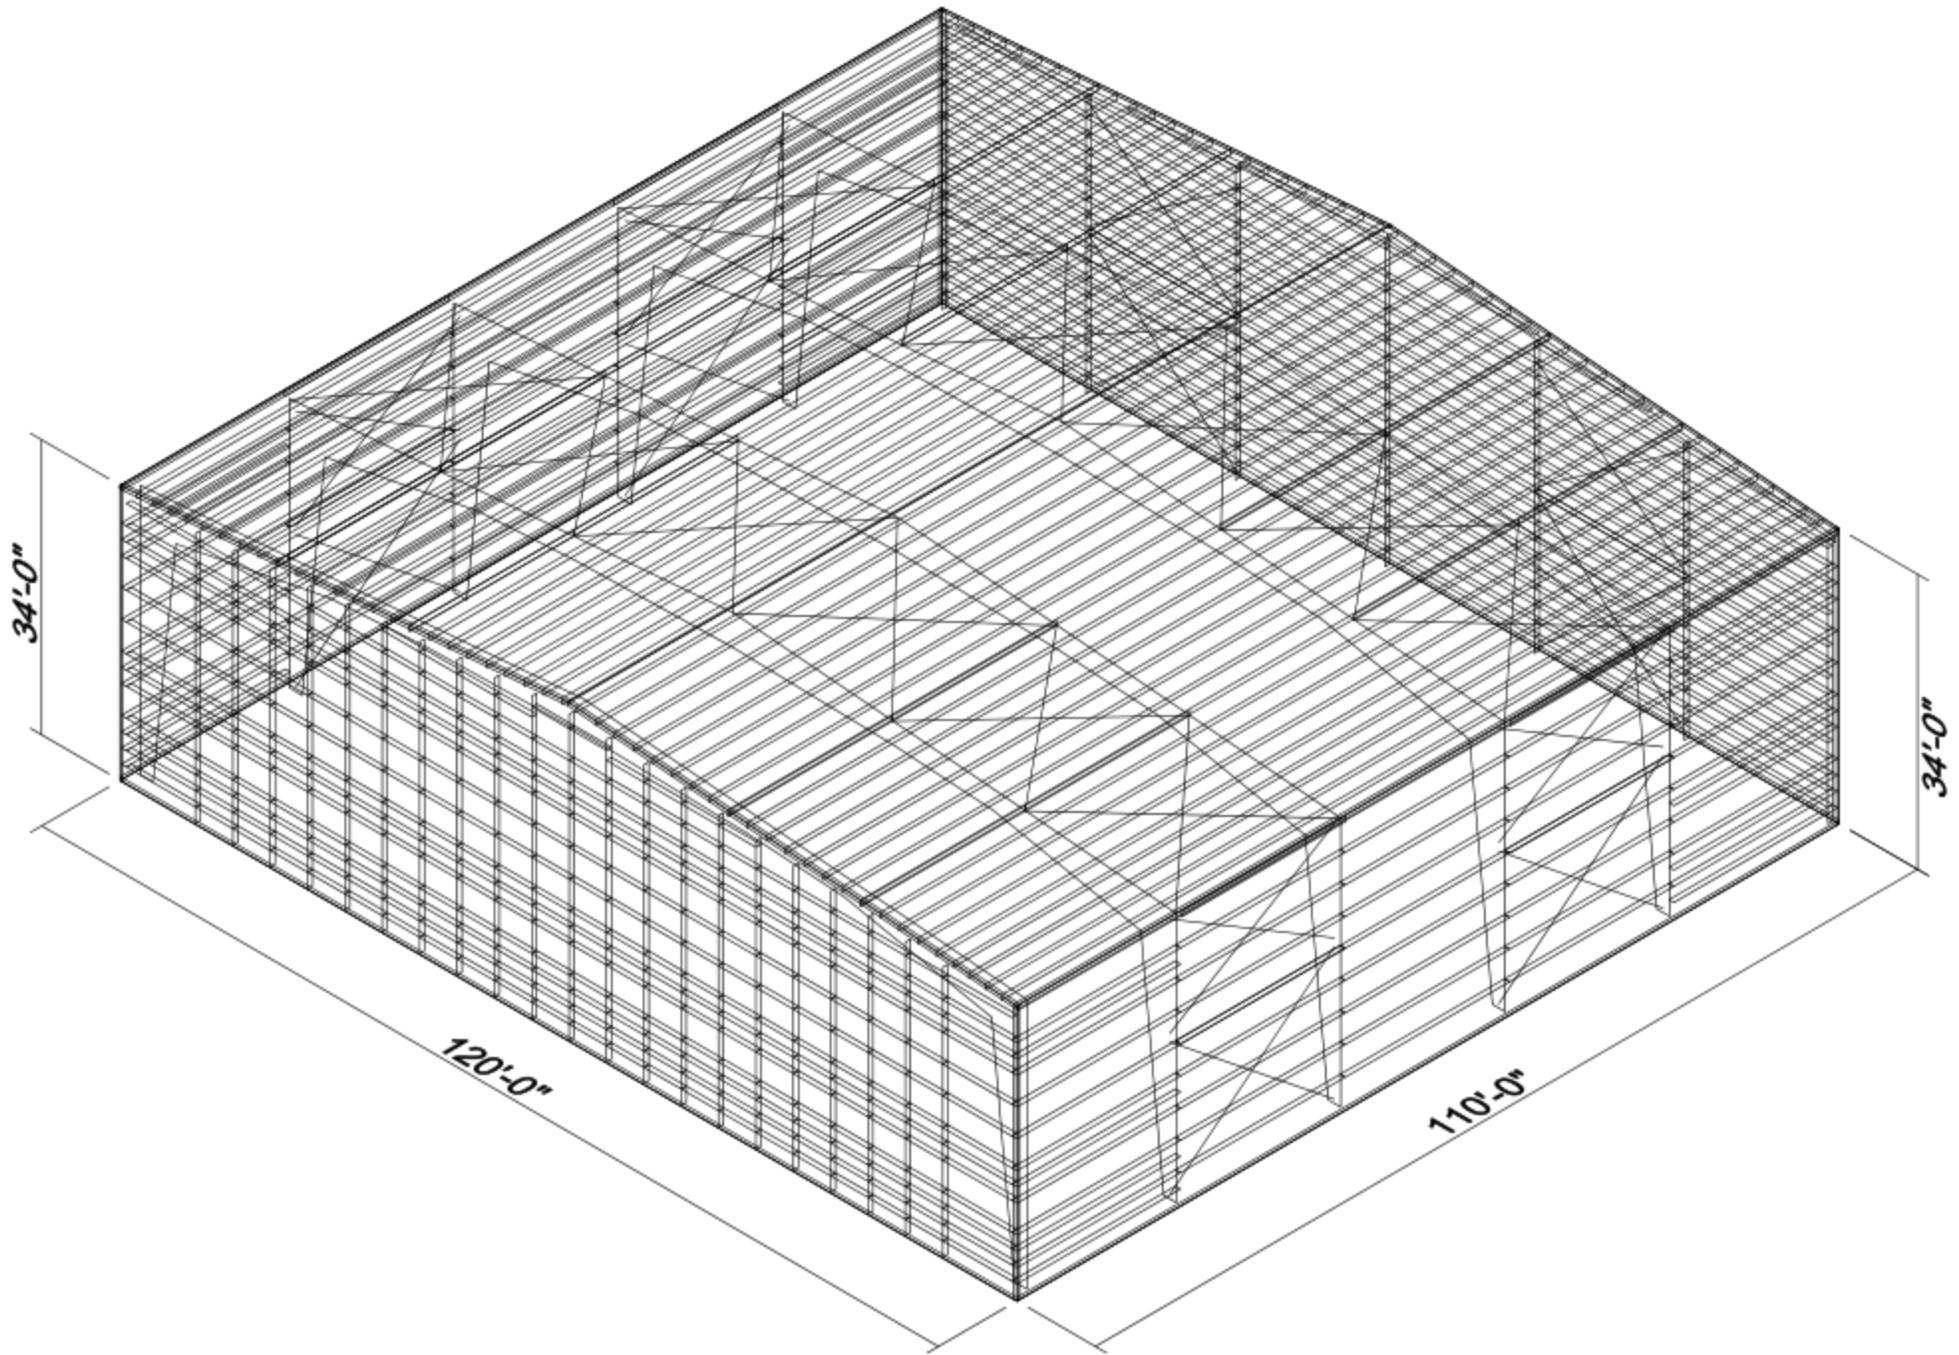


SPLICE BOLT TABLE						
Mark	Qty	Top	Bot	Int	Type	Length
SP-1	4	4	4	4	A325	1.250
SP-2	4	4	2	2	A325	0.750
SP-3	4	4	2	2	A325	0.875

BASE PLATE TABLE			
Col	Width	Thick	Length
BP-1	10"	1"	1'-10"

▽ FLANGE BRACES: Both Sides ( )  
 FB(x)(1): xx=length (1)=one side  
 C - L2.5x2.5x10ga. w/ 1/8" Flat Galvalume/Plain  
 B - L2X2X1/8

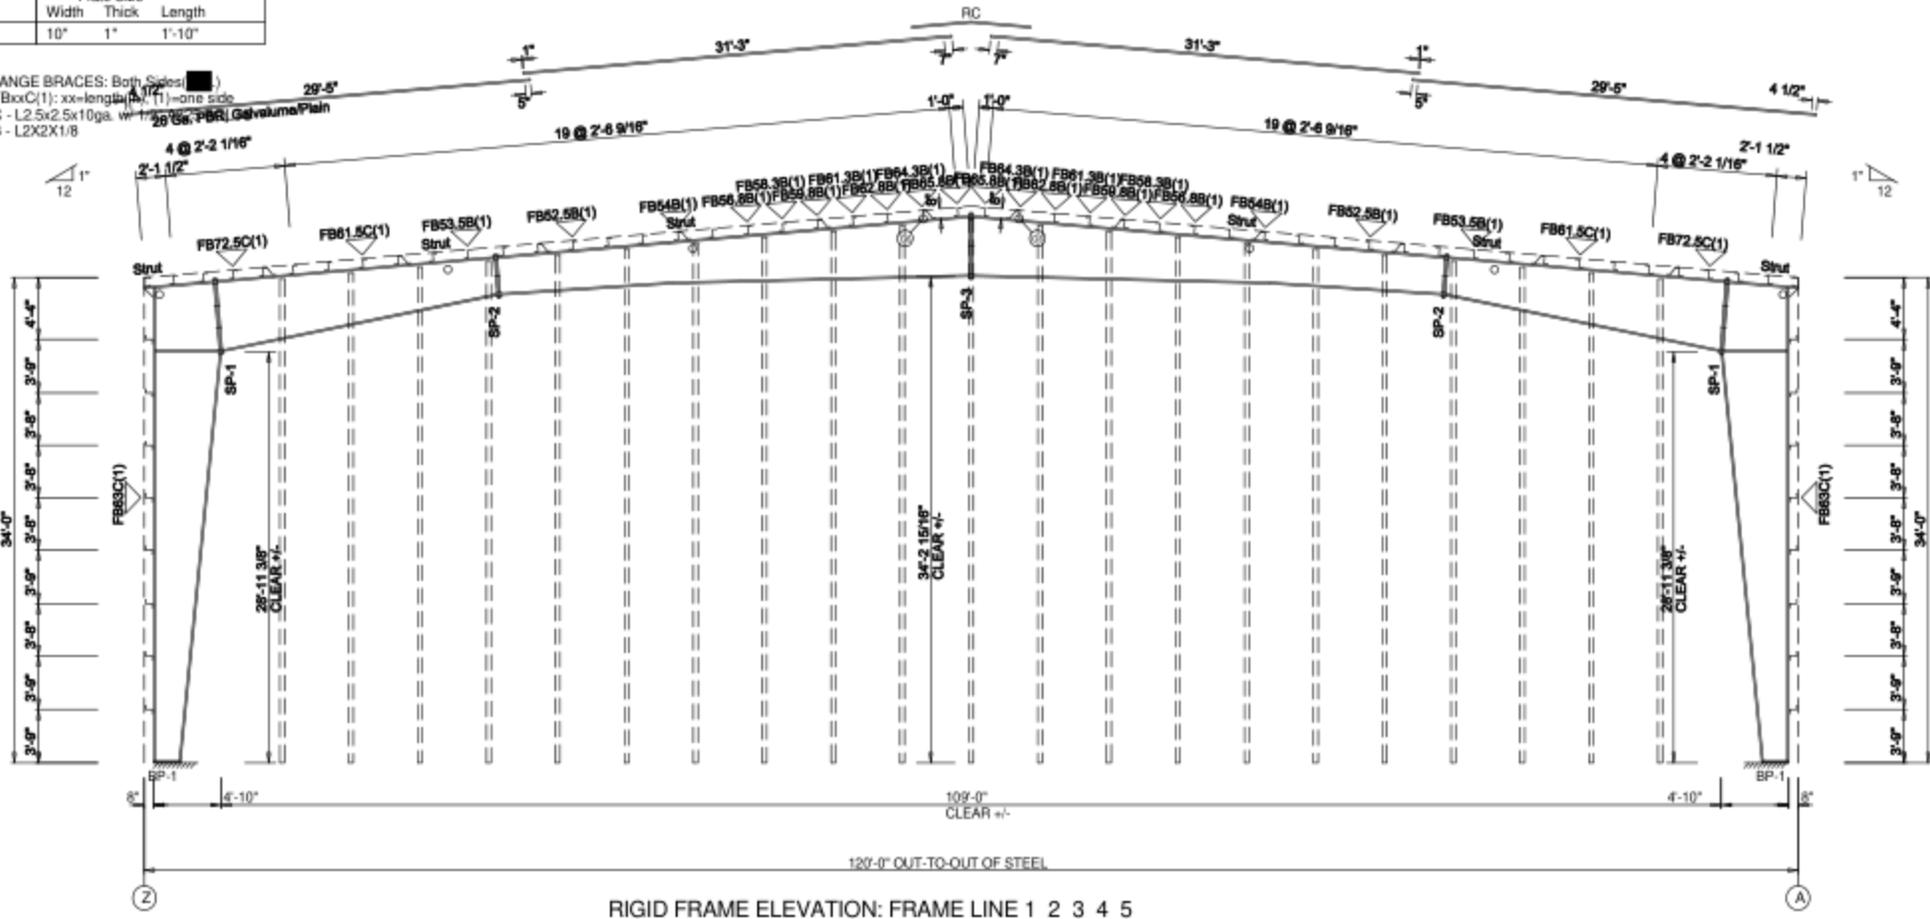

RIGID FRAME ELEVATION: FRAME LINE 1 2 3 4 5



**GENERAL NOTES:**  
 MINOR FIELDWORK OF STRUCTURAL, SECONDARY AND PANEL TRIMMING MAY BE NECESSARY TO ENSURE PROPER FIT. SUCH WORK IS CONSIDERED A NORMAL PART OF METAL BUILDING ERECTION. WE WILL NOT HONOR BACKCHARGES FOR MINOR FIELD WORK.

City:		State:		Customer:	
Designer:	Date: 8/14/13	Drafter:	Date: 8/14/13		
Detailer:	Date: 8/14/13	Office:		Job No.:	
Checker:	Date: 8/14/13	Office:		dwg	
RIGID FRAME ELEVATION					Sht. of 10
