ID	Task Name	Duration	Start	Finish
1				
2	**Design / Selection**	**15 days**	**Mon 4/18/11**	**Fri 5/6/11**
3	Site design	15 days	Mon 4/18/11	Fri 5/6/11
4	Site drains	15 days	Mon 4/18/11	Fri 5/6/11
5	Site lighting	15 days	Mon 4/18/11	Fri 5/6/11
6	Rebar	5 days	Mon 4/18/11	Fri 4/22/11
7	Shower enclosure	15 days	Mon 4/18/11	Fri 5/6/11
8	Plumbing fixtures	15 days	Mon 4/18/11	Fri 5/6/11
9	Electrical fixtures	15 days	Mon 4/18/11	Fri 5/6/11
10				
11				
12	**Pricing / Ordering**	**45 days**	**Mon 4/18/11**	**Fri 6/17/11**
13	Site design	15 days	Mon 5/9/11	Fri 5/27/11
14	Pool tile	8 days	Mon 4/18/11	Wed 4/27/11
15	Site drains	25 days	Mon 5/9/11	Fri 6/10/11
16	Coral tile	25 days	Mon 4/18/11	Fri 5/20/11
17	Site lighting	30 days	Mon 5/9/11	Fri 6/17/11
18	Rebar	10 days	Mon 4/25/11	Fri 5/6/11
19	CMU	5 days	Mon 4/18/11	Fri 4/22/11
20	Doors/Frames/Shutters	30 days	Mon 4/18/11	Fri 5/27/11
21	Interior doors	30 days	Mon 4/18/11	Fri 5/27/11
22	Finish hardware	30 days	Mon 4/18/11	Fri 5/27/11
23	Roof framing	15 days	Mon 4/18/11	Fri 5/6/11
24	Roofing assembly	20 days	Mon 4/18/11	Fri 5/13/11
25	Copper gutters	20 days	Mon 4/18/11	Fri 5/13/11
26	Shower enclosure	20 days	Mon 5/9/11	Fri 6/3/11
27	Coral flooring	25 days	Mon 4/18/11	Fri 5/20/11
28	Vanity / Tops	30 days	Mon 4/18/11	Fri 5/27/11
29	Plumbing fixtures	20 days	Mon 5/9/11	Fri 6/3/11
30	A/C Systems	30 days	Mon 4/18/11	Fri 5/27/11
31	Electrical fixtures	30 days	Mon 5/9/11	Fri 6/17/11

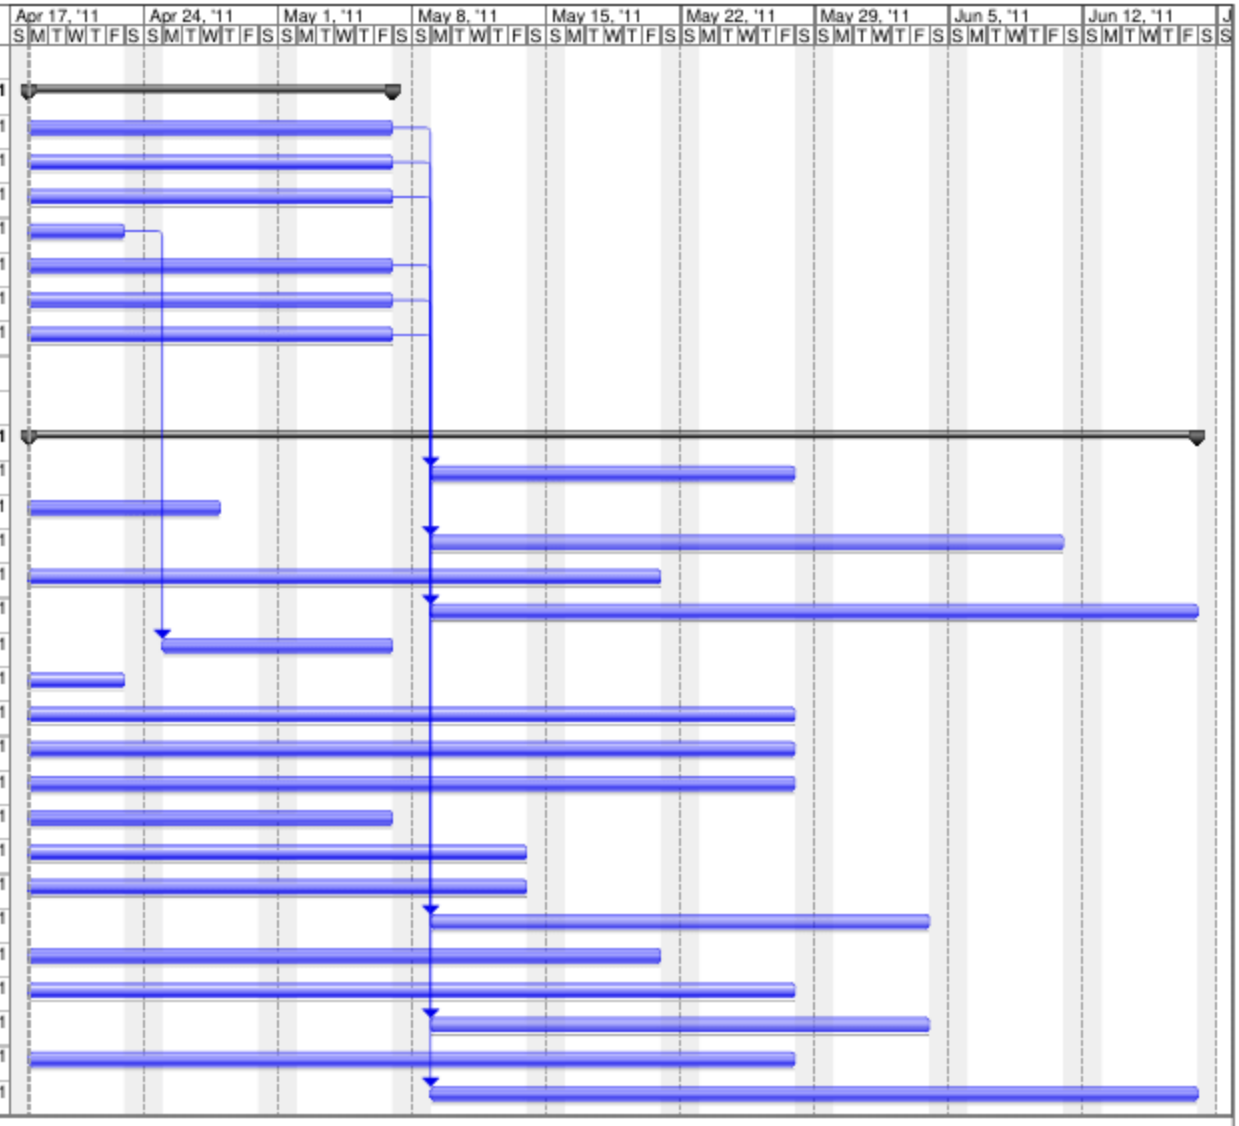

Project: Procurement MainHouse 18Ap
Date: Mon 4/18/11

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

EFTA00592281
