#1013
FLOGPOLE POOL

ID	Task Name	Duration	Start	Finish
1				
2	**Design / Selection**	**15 days**	**Mon 4/18/11**	**Fri 5/6/11**
3	Site lighting	15 days	Mon 4/18/11	Fri 5/6/11
4	Pool tiles	2 days	Mon 4/18/11	Tue 4/19/11
5	Roof tiles	5 days	Mon 4/18/11	Fri 4/22/11
6	Finish hardware	15 days	Mon 4/18/11	Fri 5/6/11
7	Shower enclosure	15 days	Mon 4/18/11	Fri 5/6/11
8	Bathroom tile	15 days	Mon 4/18/11	Fri 5/6/11
9	Flooring	15 days	Mon 4/18/11	Fri 5/6/11
10	Sun shade	15 days	Mon 4/18/11	Fri 5/6/11
11	Kitchen equipment	15 days	Mon 4/18/11	Fri 5/6/11
12	Cabinets / Tops	15 days	Mon 4/18/11	Fri 5/6/11
13	Plumbing fixtures	15 days	Mon 4/18/11	Fri 5/6/11
14	Electrical fixtures	15 days	Mon 4/18/11	Fri 5/6/11
15				
16				
17	**Pricing / Ordering**	**45 days**	**Mon 4/18/11**	**Fri 6/17/11**
18	Trench drain	20 days	Mon 4/18/11	Fri 5/13/11
19	Site lighting	10 days	Mon 5/9/11	Fri 5/20/11
20	Coral tiles	15 days	Mon 4/18/11	Fri 5/6/11
21	Pool tiles	7 days	Wed 4/20/11	Thu 4/28/11
22	Roof trusses	15 days	Mon 4/18/11	Fri 5/6/11
23	Roof tiles	20 days	Mon 4/25/11	Fri 5/20/11
24	Exterior doors	10 days	Mon 4/18/11	Fri 4/29/11
25	Interior doors	10 days	Mon 4/18/11	Fri 4/29/11
26	Finish hardware	30 days	Mon 5/9/11	Fri 6/17/11
27	Shower enclosure	20 days	Mon 5/9/11	Fri 6/3/11
28	Bathroom tile	30 days	Mon 5/9/11	Fri 6/17/11
29	Flooring	30 days	Mon 5/9/11	Fri 6/17/11
30	Hurricane shutter	15 days	Mon 4/18/11	Fri 5/6/11
31	Sun shade	30 days	Mon 5/9/11	Fri 6/17/11
32	Kitchen equipment	20 days	Mon 5/9/11	Fri 6/3/11
33	Cabinets / Tops	20 days	Mon 5/9/11	Fri 6/3/11
34	Plumbing fixtures	30 days	Mon 5/9/11	Fri 6/17/11
35	A/C Systems	30 days	Mon 4/18/11	Fri 5/27/11
36	Electrical fixtures	30 days	Mon 5/9/11	Fri 6/17/11

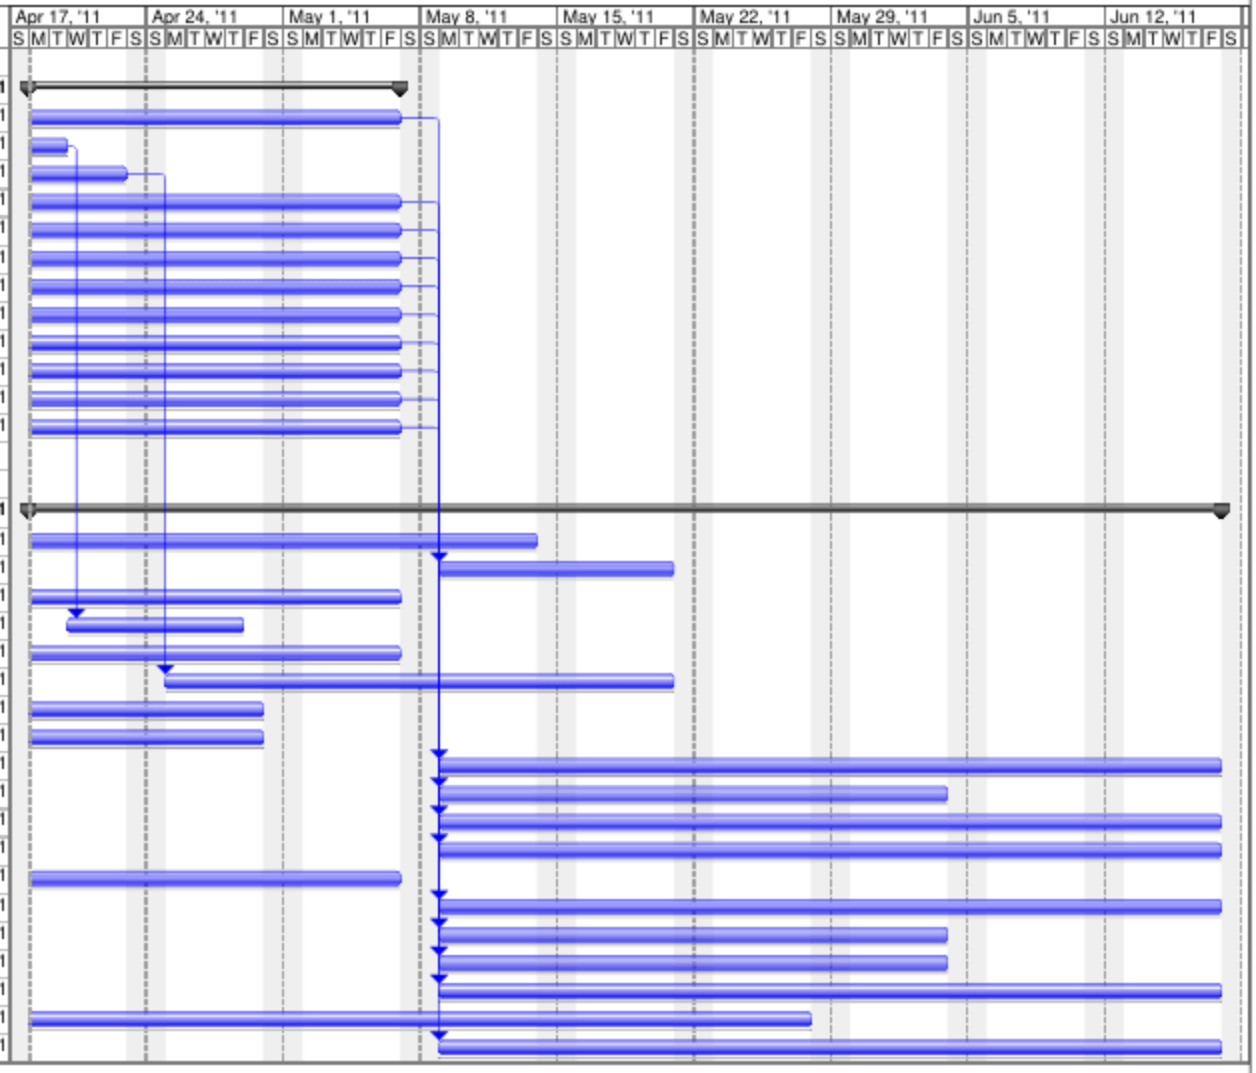

Project: Procurement 18Apr11.mpp
Date: Mon 4/18/11

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

EFTA00592282
